

Attachment 1—Overview of Programme of Works

Renovation of the Historical Buildings (Buildings A, B, C, D and S) at the Palais des Nations in Geneva, Switzerland

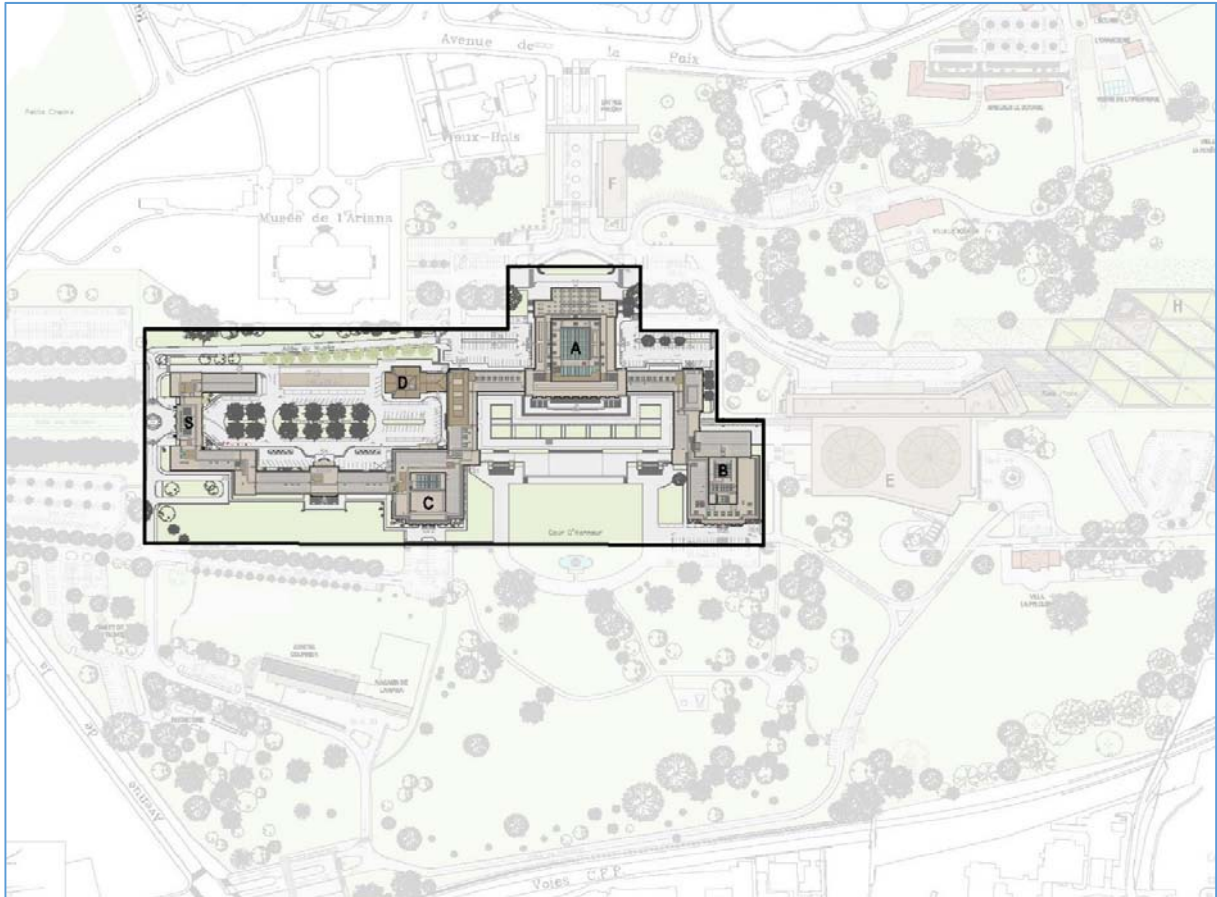


Figure 1:
Palais des Nations — overall view with enhanced view
of the buildings covered by this RFPQS

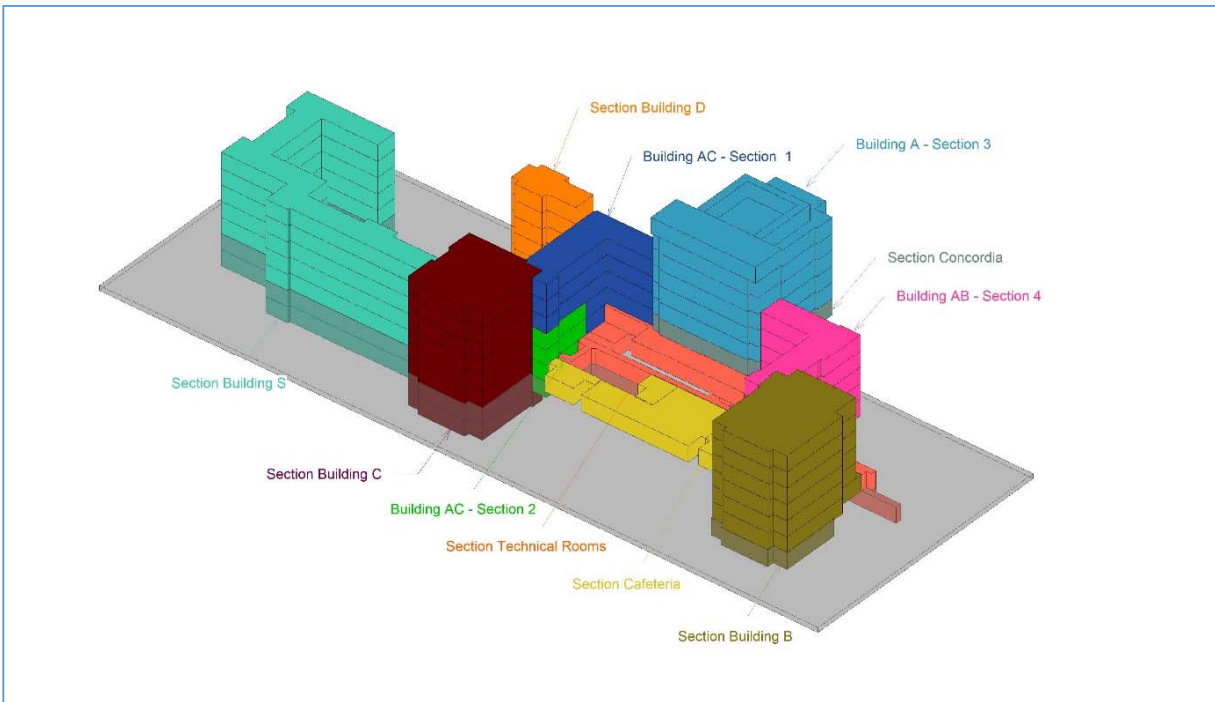


Figure 2:
3D representation of the different Sections of Work of Historical Building Renovation
(compact view — height proportion not respected)

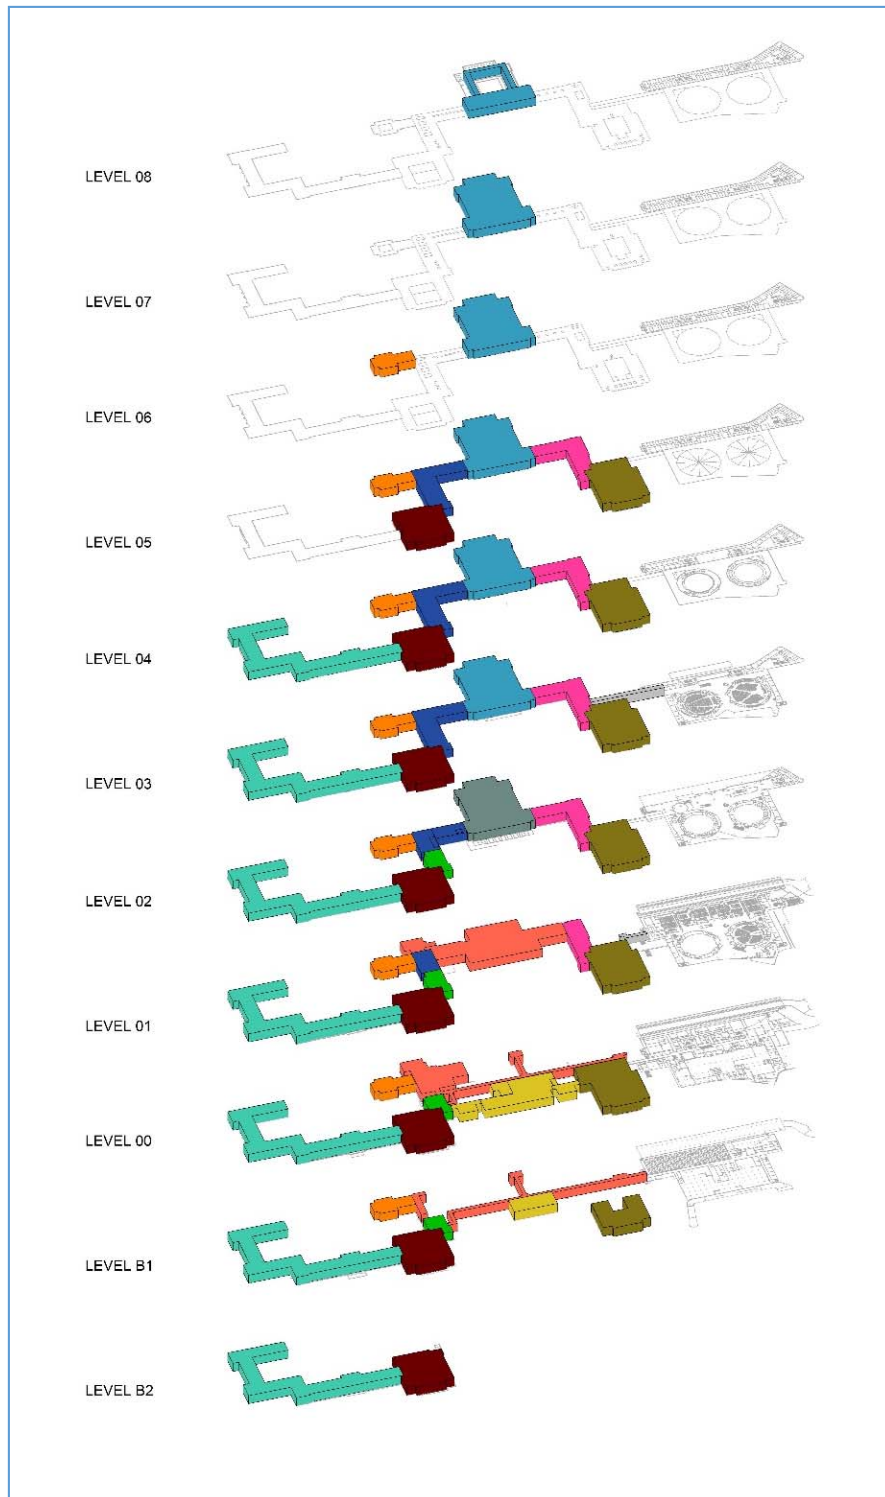


Figure 3:

3D representation of the different Sections of Work of Historical Building Renovation

(view by level)

Section	Localisation	Evaluated duration (months)	Particular constraints
Section 1	Building AC	8	Must overlap as little as possible with Section 3
Section 2	Building AC	7	Must overlap with Section Technical rooms
Section 3	Building A	12	Must overlap as much as possible with Section Technical rooms
Section 4	Building AB	12	Must overlap as little as possible with Section 3
Section Concordia	Building A	7	Must overlap with Section Technical rooms
Section C	Building C	13	Cannot begin before the New Building is available
Section D	Building D	13	Cannot begin before the New Building is available
Section S	Building S	18	Cannot begin before the New Building is available
Section B	Building B	12	Cannot begin before Section S is handed over
Section Technical Rooms	Building A	7	Must begin as soon as possible
Section Cafeteria	Building A	8	Must close activity only 3 months in summer

Table 1:
Evaluated duration of works and particular constraints for Sections of Work

Project Timeline

Activities / Year	2018	2019	2020	2021	2022	2023
<i>Contract 1 - New Building H</i>	[Grey bar]					
Contract 2 - Renovation of the Historical Building		[Green bar]				
Request For Proposal		[Green bar]				
Evaluation of proposals		[Green bar]				
Contract signature		[Green bar]				
Contractor's mobilization		[Green bar]				
Renovation works of blds. A/B/C/D/S		[Green bar]				
Final Hand Over					[Green bar]	
<i>Contract 3 - Renovation of 1970s E bldg.</i>					[Grey bar]	




UN Construction Contracts:	Firm activity:
 Contract 2 - purpose of this EOI  Contract 1 and Contract 3	 This Contract

Table 2:
SHP Global Project Timeline
